



I-215; 300 East to S.R. 201 Project Update

October 19, 2016

Completed Activities

- Asphalt resurfacing on WB I-215 from 300 East to Redwood Road
- Ramps at S.R. 201
- Ramps at 4700 South
- 3800 South SB bridge
- SB I-215 bridge demolition over S.R. 201
- Concrete paving in the median



Hydro Demolition

- 3500 South and 3800 South bridge decks
- Allows precise control
- Quicker than other methods
- Reduces dust and vibration



Bridge Demolition at S.R. 201

- Crews removed the top half of the SB I-215 bridge at S.R. 201
- New bridge to be built on-site and slid into place in 2017



Current Activities

- 3500 South bridge is currently under construction
- Ramps at 4700 South
- Ramps at S.R. 201
- Mainline SB I-215 reconstruction




Winter Operations

- Traffic Shift
- WB S.R. 201 on-ramp to SB I-215 will be closed for up to 65 days
- NB I-215 off-ramp to WB 3500 South will be closed for up to 45 days
- Concrete paving on SB I-215

Traffic Shift

- SB I-215 traffic will be in the median from S.R. 201 to 4700 South
- Drivers exiting at 3500 South must use right lanes
- Scheduled to shift in late October

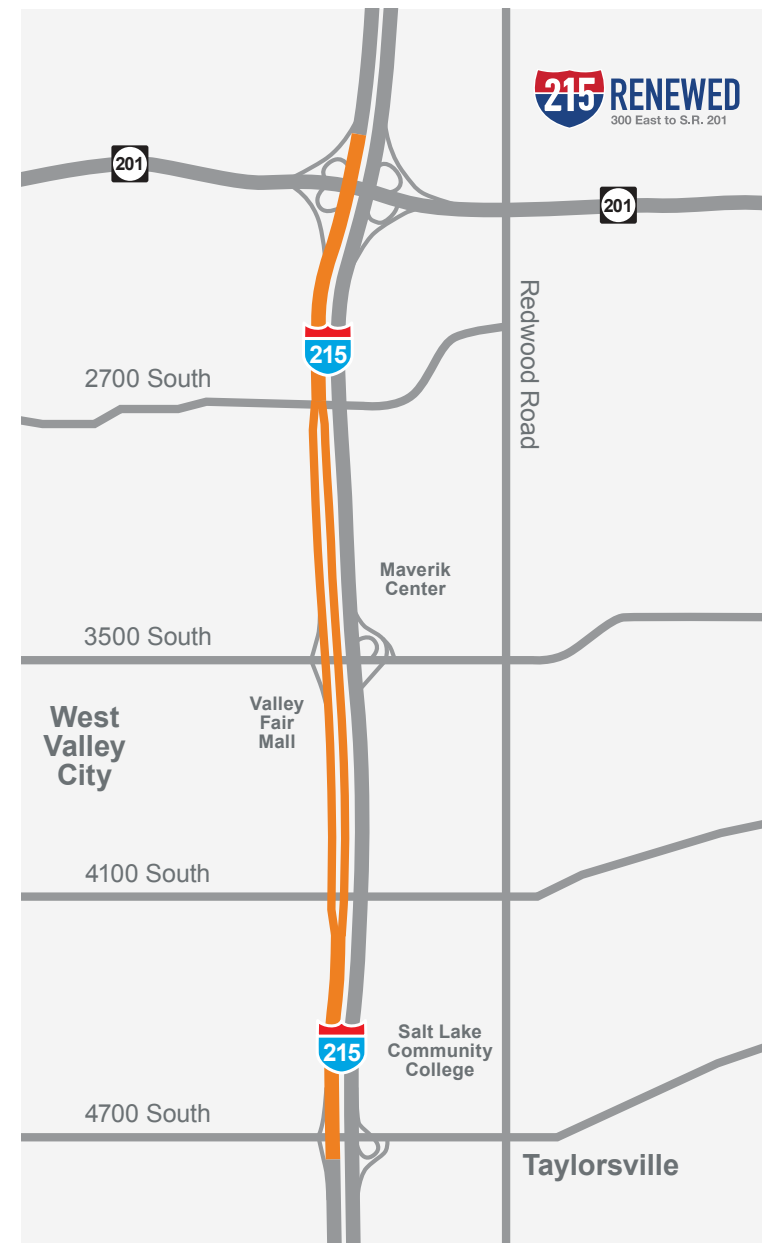

Ramp Impacts



2017 Activities

- Northbound I-215 reconstruction
- ABC bridge slide at S.R. 201
- Additional ramp improvements

Questions or Comments
